



City of San Leandro

Meeting Date: March 7, 2016

Staff Report

File Number: 15-733 **Agenda Section:** CONSENT CALENDAR

Agenda Number: 8.D.

TO: City Council

FROM: Chris Zapata
City Manager

BY: Keith Cooke
Engineering & Transportation Director

FINANCE REVIEW: David Baum
Finance Director

TITLE: Staff Report for a Resolution Accepting the Work for the Fiber Conduit for
Broadband Network Project, Project No. 2013.0320

SUMMARY AND RECOMMENDATIONS

Staff recommends that the City Council accept the work and authorize the City Manager to file the Notice of Completion, release the performance and payment bonds, and release the maintenance bond upon successful completion of the one-year maintenance period.

BACKGROUND

In partnership with Lit San Leandro and to promote business growth in the local area, high speed communication infrastructure was expanded into underserved industrial areas of the City, primarily the Adams Tract, Catalina/Farallon area, and the southern Alvarado corridor. The City received grant funding from the United States Economic Development Agency (EDA) for the installation of communication conduits.

The project expanded the City's communications network capability by installing approximately eight and a half miles of conduit ready to receive fiber optic cables. The City's fiber optic conduit network now exceeds 26 miles (see attached map).

A favorable bidding environment allowed this project to be completed under budget and add additional conduit alignments into the project scope. A contract change order enabled an increase from 7.5 to 8.5 miles of installed conduit and at completion, the project remained under budget. Remaining grant funds will be used in a subsequent project to further increase the fiber optic conduit network.

In addition to promoting growth and creating jobs in the industrial sector, the extensive conduit network infrastructure also provides the opportunity for schools, the community and businesses throughout the city to easily and readily connect to high speed internet communication service. The planning, investment and effort placed in building the network is

second to none in similar communities in and beyond the San Francisco Bay Area and provides the potential for citizens, businesses and visitors to thrive in the digital environment and help keep our community on the cusp of innovation.

Analysis

Construction is complete. The work was inspected and deemed to comply with the contract documents and City standards.

Previous Actions

- On July 7, 2014 by Resolution No. 2014-068, the City Council awarded a contract for construction of the work to Flatiron Electric Group, Inc.
- On June 15, 2015 by Resolution No. 2015-107, the City Council increased the construction contract change order cap from 25% to 40%.

Permits and/or Variances Granted

A Caltrans Encroachment permit was issued for the segment of work within the State right of way.

Union Pacific Railroad issued Wireline Crossing Agreements for the locations where the project crossed railroad right of way.

Environmental Review

The project was determined categorically exempt pursuant to subsection 15304(f), 'Minor Alteration to Land' of the California Environmental Quality Act (CEQA) guidelines.

Fiscal Impacts

A summary of the construction contract with Flatiron Electric Group, Inc., is below:

Original Contract	\$1,325,350.00
Change Orders	<u>\$ 418,798.11</u>
Total Contract Amount	\$1,744,148.11

The contractor submitted a claim in the amount of \$113,000.00 for work they believe is an extra to the contract. The claim will be handled in accordance with the terms of the contract.

The project cost is \$2,173,798.00, including design and construction administration (including the full claim allowance of \$113,000).

Budget Authority


The total appropriation for the Project is funded from the following sources:

- \$2,121,000 EDA Grant funds in account 150-38-347 appropriated as part of the Fiscal Year 2012-13 budget.
- \$150,000 Developer Fees for Street Improvements (DFSI) funds in account 120-38-347 appropriated as part of the Fiscal Year 2012-13 budget.
- \$352,000 General Funds in account 210-38-347 appropriated as part of the Fiscal Year 2012-13 budget.


ATTACHMENT

- Fiber Optic Conduit Network Map

PREPARED BY: John O'Driscoll, Associate Engineer, Engineering and Transportation Department

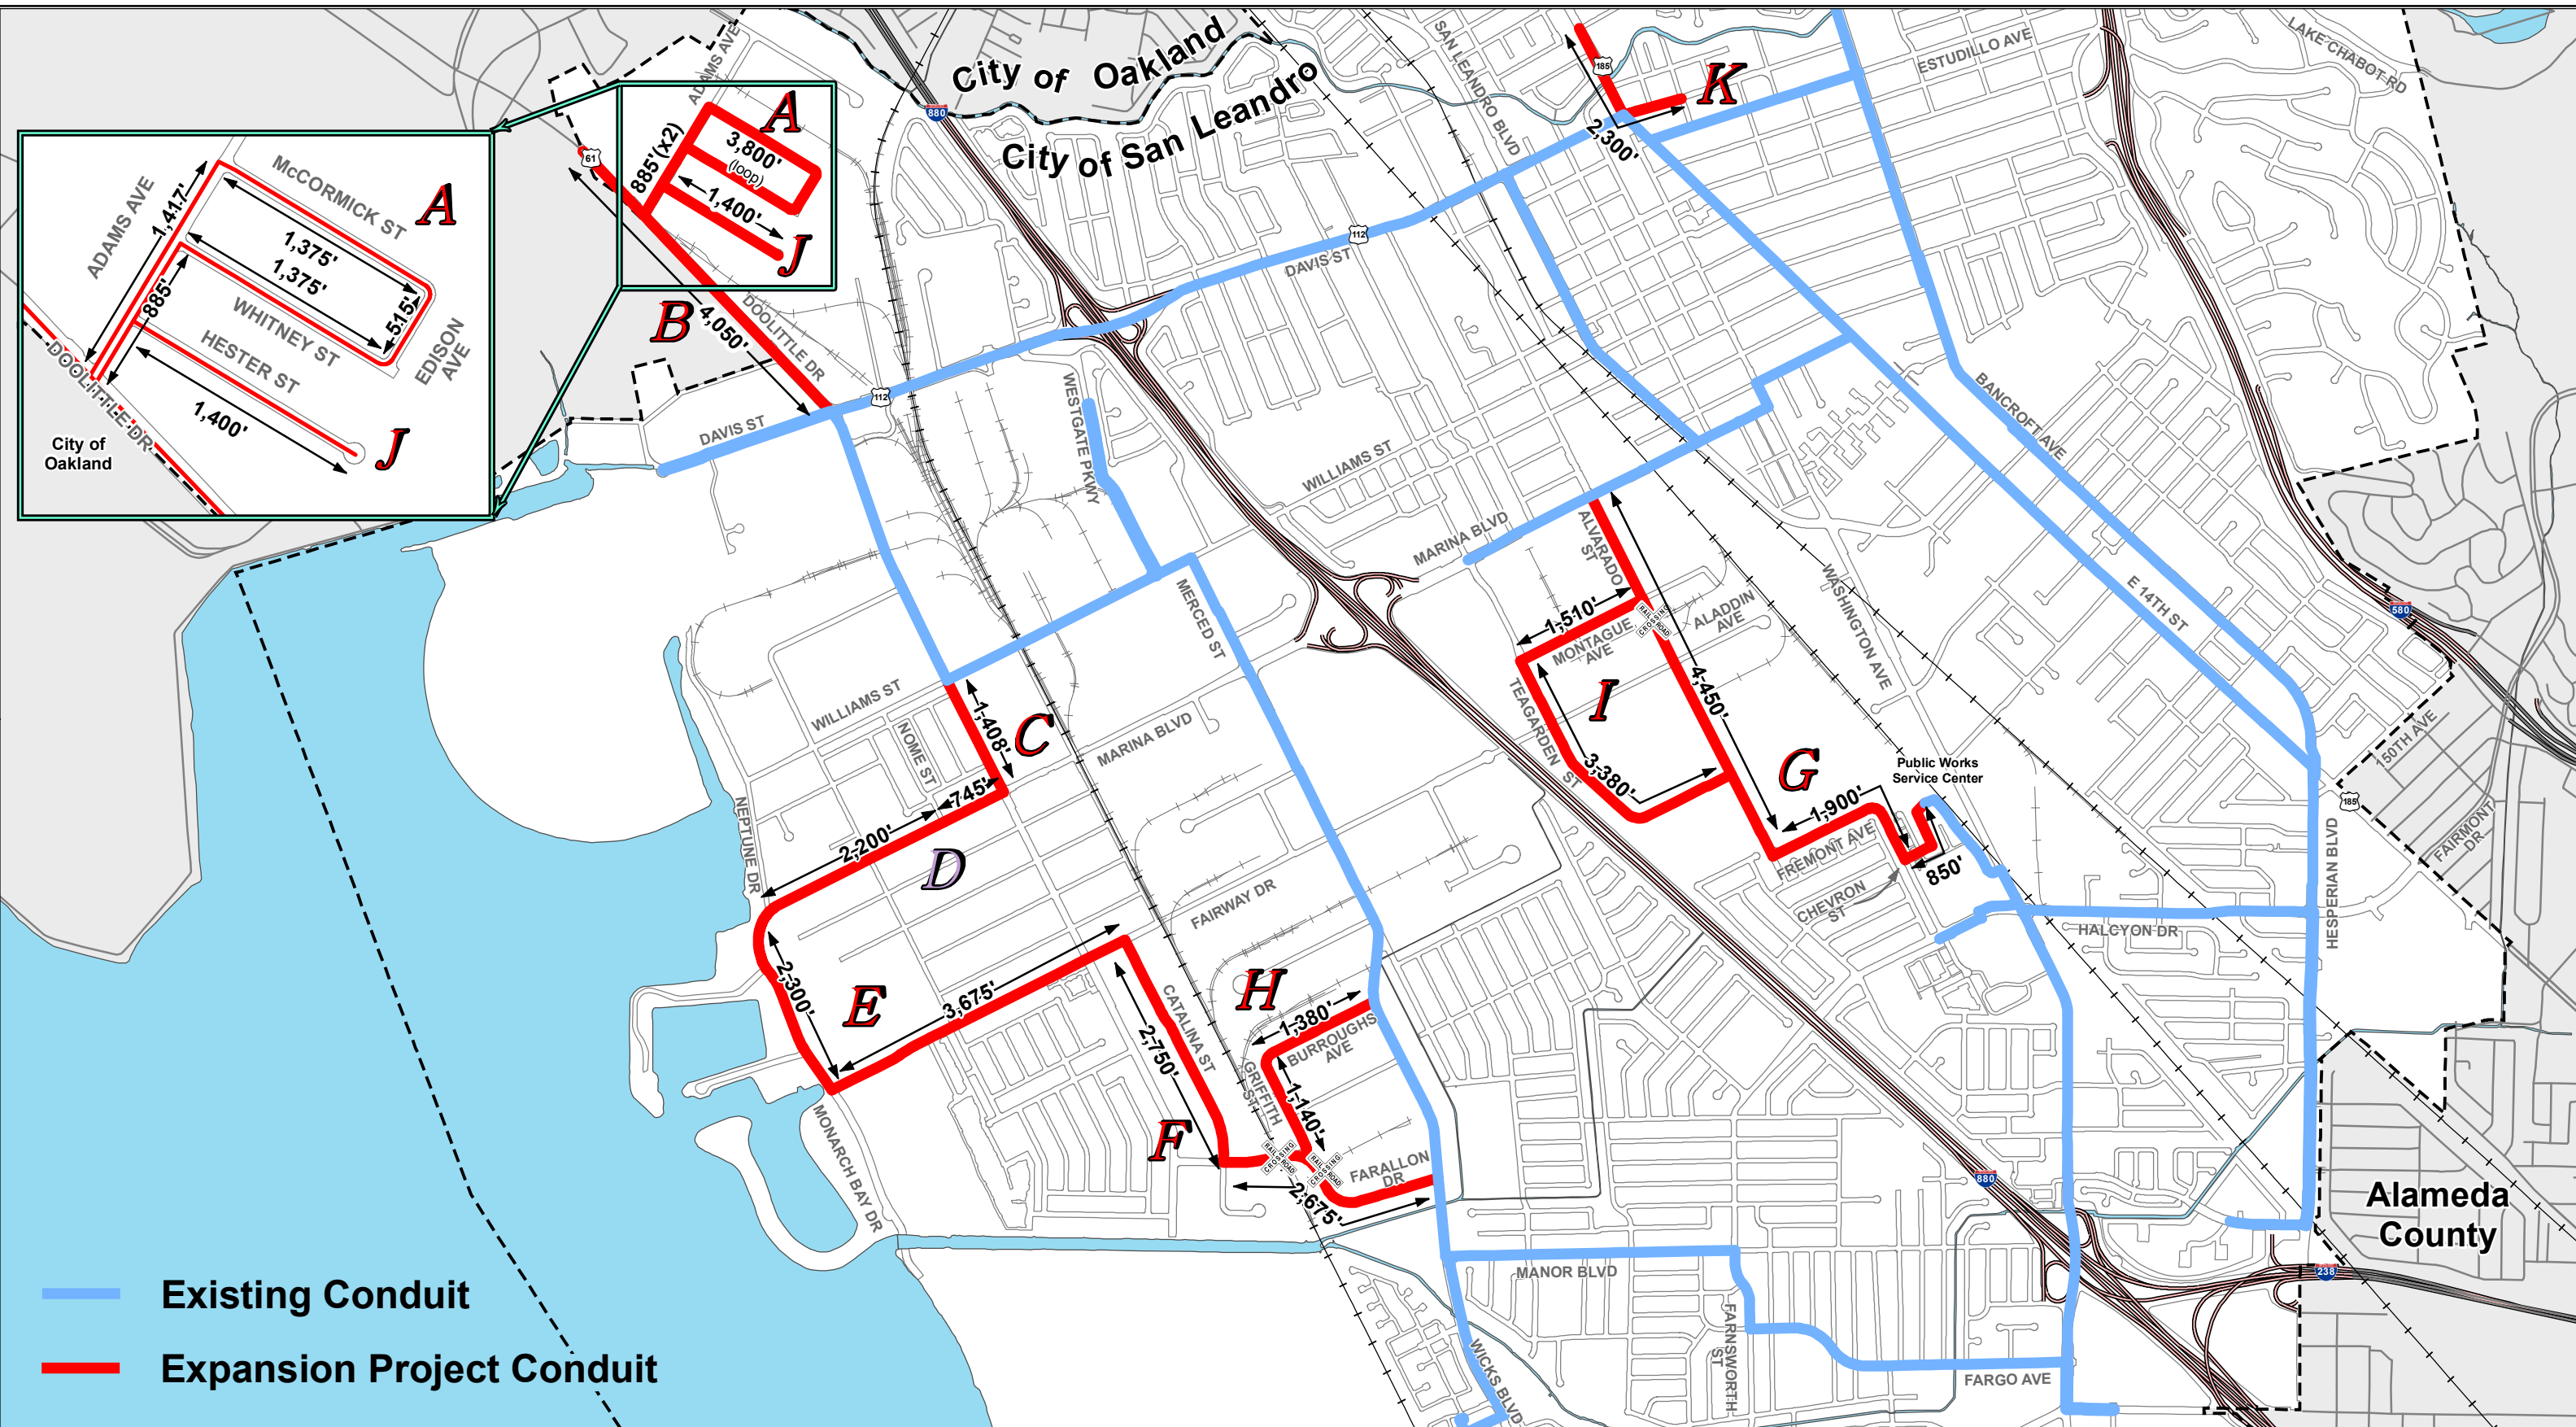

San Leandro Fiber Optic Conduit Network





City of San Leandro

Meeting Date: March 7, 2016

Resolution - Council

File Number: 15-734

Agenda Section: CONSENT CALENDAR

Agenda Number:

TO: City Council

FROM: Chris Zapata
City Manager

BY: Keith Cooke
Engineering & Transportation Director

FINANCE REVIEW: David Baum
Finance Director

TITLE: RESOLUTION Accepting the Work for Fiber Conduit for Broadband Network Project, Project No. 2013.0320 (provides for acceptance of work for the Fiber Conduit for Broadband Network Project funded with Grants from the Economic Development Agency)

WHEREAS, pursuant to a construction contract between the City of San Leandro and Flatiron Electric Group, Inc. approved on July 7, 2014 by Resolution No. 2014-068, Flatiron Electric Group, Inc. has completed the Fiber Conduit for Broadband Network; and

WHEREAS, said work was completed in accordance with the plans and specifications and to the satisfaction of the Engineering and Transportation Director, who therefore recommends that said work be accepted.

NOW, THEREFORE, the City Council of the City of San Leandro does RESOLVE as follows:

1. That the work hereinbefore described is hereby accepted; and
2. That the City Clerk is hereby directed to file a Notice of Completion on said project; and
3. That the bonds heretofore given for performance and payment of said conditions are hereby discharged and exonerated from further liability when the statute of limitations expires after the recording of the Notice of Completion; and
4. That upon completion of the one-year maintenance period established pursuant to said contract, and to the satisfaction of the Engineering and Transportation Director, the City Manager is hereby authorized to release the maintenance bond heretofore given for maintenance of the work hereinbefore described.
